


FACTS AND FIGURES



Damage Status - Private Structures

MAJOR HOUSING TYPOLOGIES

Typology	Municipal	District
Stone and Mud Mortar Masonry	97.14%	92.87%
Timber Frame Structure	1.19%	1.06%
Bamboo	0.68%	0.73%
Adobe Structures	0.58%	4.33%
Others	0.41%	0.99%

CBS damage assessment survey, 2015

HOUSING RECONSTRUCTION & RETROFIT UPDATES

Reconstruction Status

Total Eligible HHs	2,977
PA Agreement	2,889 (88)
I st Tranche received	2,888 (89)
II nd Tranche received	2,561 (416)
III rd Tranche received	2,287 (690)

Houses

Under Construction: 2,561

Completed: 2,287

Retrofitting Status

Total Eligible HHs	469
PA Agreement	247 (222)
I st Tranche received	247 (222)
II nd Tranche received	469

Grievances

Registered: 1,344

Addressed: -

Non-compliances

Registered: -

Addressed: -

Data Updated on: 2019-04-22 00:00:00

PO Presence

Active: No POs Reported

Phased Out: ACTED (Shelter), GON (Shelter), HELVETAS (Shelter), NRCS (Agriculture), NRCS (Education), NRCS (Livelihood), NRCS (Health), NRCS (Shelter), NRCS (Hygiene), RCJ (Education)

STATUS OF CONSTRUCTION MATERIALS

Materials	Unit	Req. Quantity*	Ava.	Cost (NRs.)**
Stone	m ³	49,858	Y	7,000
Aggregate	m ³	47,551	Y	-
Sand	m ³	5,289	-	-
Timber	cu. ft.	5,976	-	1,450
Cement (PPC)	Sack	-	Y	1,050
Cement (OPC)	Sack	157,253	Y	1,150
Rebars	kgs.	544,691	-	100
Tin	bundle	6,416	-	10,500
Bricks	pcs.	620,256	-	26

Types of Workers

1. Skilled mason
2. Labourer

Avg. daily wage (NRs.)

1,200 /-
1,000 /-

OTHER SECTORS



Schools

Damaged: 61
Under Construction: 13
Construction Completed: 13



Health Posts

Damaged: -
Under Construction: -
Construction Completed: -

KEY CONTACTS

Municipal Office

Mani Raj Rai
Chairman
9841535837

Municipal Office

Indra Jit Yadav
Focal Person
9826722669

Municipal Office

Hem Kumari Tamang
Deputy Chairman
9842967190

DLPIU-GMaLI

Yubaraj Kharel
DLPIU-Chief
9852841350

Municipal Office

Samser Bdr Rai
Chief Administration Officer
9852840501

DLPIU-Building

Pravakar Lal Karn
DLPIU-Chief
9841507715

HHs WITH LAND ISSUES

No Reported Land Issues


STATUS OF TECHNICAL STAFF

Staff	Available Nos.	Additional Req. Nos.
Engineers	-	-
Sub-Engineers	-	-
Asst. Sub-Engineers	-	-
Masons	- (7 days) - (50 days)	- (7 days) - (50 days)

Source: Municipal survey


MASON TRAINING

Trainings (# out of total required)



Source: HRRP Analysis

TA ACTIVITIES MAP

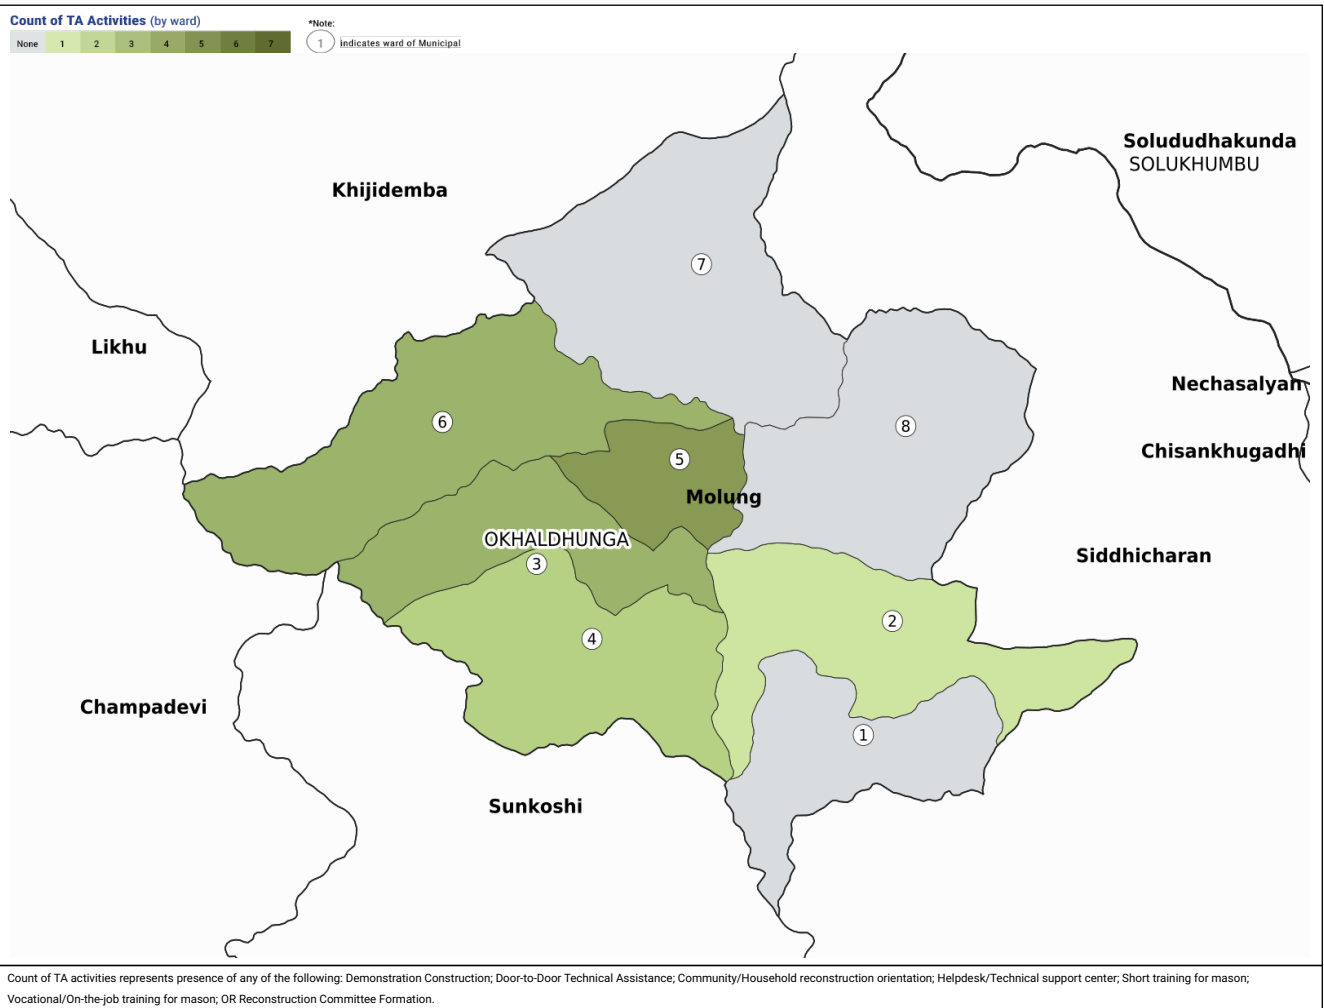

FAQs

Q: What documents are required for enrolment in the GoN housing reconstruction programme?

A: Two copies of passport size photos and original copy and photocopy of land ownership card and citizenship card. Local officials at the Rural / Urban Municipality will be able to provide information and support and households can enrol at the Rural / Urban Municipality.

Q: Do we need to pay the engineers when they come to conduct inspections or provide technical assistance?

A: No, you do not have to pay the engineers, or any other staff, conducting inspections or providing technical assistance. If any field staff request payment for conducting inspection or providing technical assistance you should report it to the Rural / Urban Municipality officials.

For further information 1. Prakash Basnet (District Coordinator) 9851154315 2. (District Technical Officer) 3. Birodh Kattel (District Information Management Officer) 9841419970
